



Visit the project website
to learn more:



Construction Update - August 29, 2024

Over the last two weeks, the contractor completed watermain improvements on 7th Street, 8th Street, and 3rd Street, connecting the new pipes to the existing water system. Additionally, the contractor installed sanitary sewer service at the Burger King.

Over the next two weeks, the contractor will continue watermain and storm sewer installation in front of the fire station and BMO Harris Bank. The watermain is currently scheduled to be filled, tested and chlorinated by the week of September 9th, at which time service transfers may begin.

Any impacts to traffic or lane closures will be shared daily. Please use caution when traveling through the area.

Businesses are open during construction and access to driveways will be maintained throughout construction!




Watermain installation along Illinois Route 7



Project Map Area

The map below shows where the project is taking place.

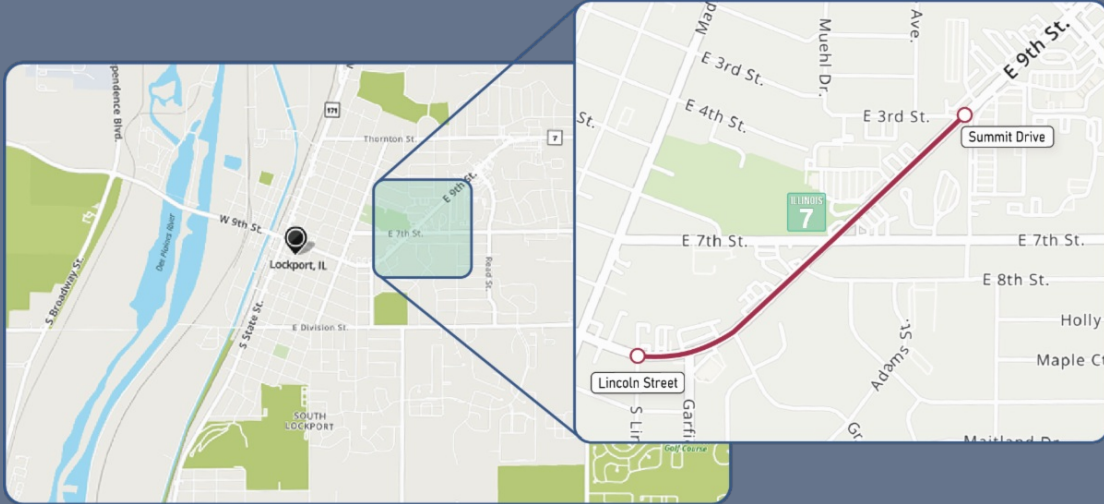

Have Questions?



Christopher B. Burke Engineering, Ltd.
Dan Schroeder, PE
Phone: (224) 315-0185
Email: dschroeder@cbbel.com



City of Lockport
Phone: (815) 838-0549
Monday - Friday 7:00am - 3:30pm
CityofLockport.net

© Copyright 2024 City of Lockport, Illinois

Metro Strategies Group | 1901 Butterfield Rd., Suite 260 | Downers Grove, IL 60515 US

[Unsubscribe](#) | [Update Profile](#) | [Constant Contact Data Notice](#)



Try email marketing for free today!
